CONSTRUCTION UPDATE BY TYLER SUPALLA, SUPERVISOR

Hidden Creek Reserve

Townhomes in Shawnee, Kansas

Last updated Thu, Nov 5 at 4:30 PM Central

Footings for Lots 19-22 are scheduled to pour today, pier pouring is starting on Lots 23-26, and backfill on the first building is planned for early next week.

LATEST FROM THE SITE

Thursday, November 5

- **Lots 11-14** · gravel for the slab base was delivered. Backfill is planned for Monday or Tuesday, Nov 9-10, so plumbing work can resume Wednesday, Nov 11.
- **Lots 19-22** · the footing pour is scheduled for this afternoon.
- **Lots 23-26** · pier pouring is starting.
- **Lots 27-30** · pier drilling is starting, and gravel for the construction driveway was delivered.

16
homes under construction
in 4 buildings, all at the foundation stage

Nov 5
Pour footings
Lots 19-22, thursday

Weekly recap

Foundation work moved forward on four buildings despite rain, with dampproofing on Lots 11-14, footing and pier pours scheduled on Lots 19-26, and the next four buildings staked and being graded.

THIS WEEK

- **Lots 11-14** · Dampproofing started Wednesday, and gravel for the slab base was delivered Thursday. Backfill is now planned for early next week.
- **Lots 15-18** · Wall forms nearly finished. The wall pour is planned Thursday at the earliest, more likely Friday.
- **Lots 19-22** · Footing forms went in Wednesday, and the footing pour was scheduled for Thursday afternoon.
- **Lots 23-26** · Pier drilling wrapped up after rain delays, and pier pouring was set to start Thursday.

NEXT WEEK

- **Lots 11-14** · Backfill planned Monday or Tuesday, with plumbing work resuming Wednesday.
- **Lots 27-30** · Continue pier drilling.
- **Lots 27-42** · Silt fencing along the driveways.

- **Lots 27-42** · All four buildings staked by the surveyor and grading started Wednesday. Pier drilling on Lots 27-30 was set to start Thursday.

The buildings



Plans · Permitted · Under construction · Complete · Not yet started

Lots 11-14

Foundation

Fourplex · 4 homes · 6704–6710 Meadowsweet Ln

Progress about 8%

Foundation · Framing · Roof · Drywall · Finishes

Dampproofing started on Nov 4 and gravel for the slab base was delivered Nov 5. Backfill is planned for Nov 9-10, with plumbing work resuming Nov 11.

Updated Nov 5, 2026

Lots 15-18

Foundation

Fourplex · 4 homes · 6716–6722 Meadowsweet Ln

Progress about 8%

Foundation · Framing · Roof · Drywall · Finishes

Crews are finishing the foundation wall forms after rain slowed work. The wall pour is planned for Thursday, Nov 5 at the earliest, more likely Friday, Nov 6.

Updated Nov 4, 2026

Lots 19-22

Foundation

Fourplex · 4 homes · 6728–6734 Meadowsweet Ln

Progress about 8%

Foundation Framing Roof Drywall Finishes

Piers are finished. The footing pour is scheduled for Nov 5.

Updated Nov 5, 2026

Lots 23-26

Foundation

Fourplex · 4 homes · 6740–6746 Meadowsweet Ln

Progress about 8%

Foundation Framing Roof Drywall Finishes

Pier drilling is wrapping up and pier pouring is starting on Nov 5.

Updated Nov 5, 2026

Lots 27-30

Plans

Fourplex · 4 homes · 6752–6758 Meadowsweet Ln

Progress about 0%

Foundation Framing Roof Drywall Finishes

Staked by the surveyor and grading started Nov 4. Gravel for the construction driveway was delivered and pier drilling is starting on Nov 5.

Updated Nov 5, 2026

Lots 31-34

Plans

Fourplex · 4 homes · 6808–6814 Meadowsweet Ln

Progress about 0%

Foundation Framing Roof Drywall Finishes

Staked by the surveyor, and grading started Nov 4.

Updated Nov 4, 2026

Lots 35-38

Plans

Fourplex · 4 homes · 6822–6828 Meadowsweet Ln

Progress about 0%

Foundation Framing Roof Drywall Finishes

Staked by the surveyor, and grading started Nov 4.

Updated Nov 4, 2026

Lots 39-42

Plans

Fourplex · 4 homes · 6834–6840 Meadowsweet Ln

Progress about 0%

Foundation Framing Roof Drywall Finishes

Staked by the surveyor, and grading started Nov 4.

Updated Nov 4, 2026

Schedule


BUILDING	FOUNDATION	FRAMING	ROOF	DRYWALL	FINISHES
Lots 11-14 about 8% complete	**In progress** Started Oct 22 Backfill planned Nov 9-10	*Not started*	*Not started*	*Not started*	*Not started*
Lots 15-18 about 8% complete	**In progress** Started Oct 22 Wall pour target Nov 5-6	*Not started*	*Not started*	*Not started*	*Not started*
Lots 19-22 about 8% complete	**In progress** Started Oct 26 Footing pour scheduled Nov 5	*Not started*	*Not started*	*Not started*	*Not started*
Lots 23-26 about 8% complete	**In progress** Started Oct 28 Pier pour starting Nov 5	*Not started*	*Not started*	*Not started*	*Not started*
Lots 27-30 about 0% complete	*Not started* Pier drilling starting Nov 5	*Not started*	*Not started*	*Not started*	*Not started*
Lots 31-34 about 0% complete	*Not started*	*Not started*	*Not started*	*Not started*	*Not started*
Lots 35-38 about 0% complete	*Not started*	*Not started*	*Not started*	*Not started*	*Not started*
Lots 39-42 about 0% complete	*Not started*	*Not started*	*Not started*	*Not started*	*Not started*

Actual dates are the first and last days the field notes record the work. Target dates appear as the master schedule fills in. Percent complete is a rough estimate by phase.

Jobsite photos



Lots 11-14 · Nov 5

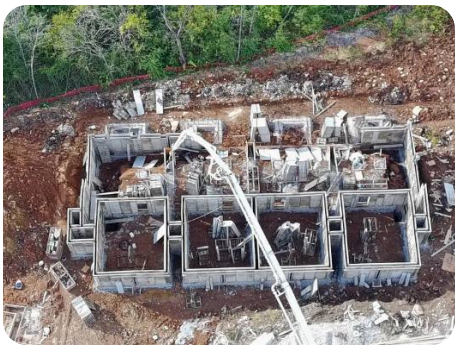

Lots 15-18 · Nov 5



Lots 15-18 · Nov 5



Lots 19-22 · Nov 5



Lots 23-26 · Nov 5



Lots 11-14 · Nov 4

Coming up

Thursday
Nov 5

Lots 19-22
Pour footings

Lots 23-26
Begin pouring foundation piers

Lots 27-30
Begin drilling foundation piers

Friday
Nov 6

Lots 15-18
Pour foundation walls (Thursday at the earliest, more likely Friday)

Monday
Nov 9

Lots 11-14
Backfill around the foundation (Monday or Tuesday)

Wednesday Nov 11	Lots 11-14	Plumbing work resumes after backfill
Date to be set when crews confirm	Lots 27-42	Install silt fencing along the driveways

Hidden Creek Reserve is a 59-home townhome community with a clubhouse, built in fourplex, triplex and duplex buildings. This page updates each weekday evening from the supervisor's field notes and jobsite photos.
