CONSTRUCTION UPDATE BY TYLER SUPALLA, SUPERVISOR

Hidden Creek Reserve

Townhomes in Shawnee, Kansas

Last updated Mon, Nov 9 at 2:31 PM Central

The Lots 15-18 foundation walls were poured Saturday, backfill is under way on Lots 11-14, and the Lots 27-30 piers are nearly ready to pour.

LATEST FROM THE SITE

Monday, November 9

- **Lots 11-14** · backfill started today, with plumbing work planned for Wednesday.
- **Lots 15-18** · foundation walls were poured Saturday, and crews started stripping the forms today.
- **Lots 19-22** · wall forms move here next, with the wall pour expected Monday, Nov 16.
- **Lots 23-26** · the footing pour may happen Wednesday.
- **Lots 27-30 and 39-42** · Lots 27-30 piers should be ready to pour Tuesday, and grading for Lots 39-42 is planned so pier drilling can start there Wednesday.

20
homes under construction
in 5 buildings, all at the foundation stage

Nov 10
Finish stripping the wall forms
Lots 15-18, tuesday

Weekly recap

The week opened with backfill on Lots 11-14 and form stripping on Lots 15-18 after Saturday's wall pour, while piers and grading move ahead on the next buildings.

THIS WEEK

- **Lots 11-14** · Backfill started Monday, with plumbing work planned for Wednesday.
- **Lots 15-18** · Walls were poured Saturday, and form stripping started Monday.
- **Lots 23-26** · Footing pour planned for Wednesday.

NEXT WEEK

- **Lots 19-22** · Foundation wall pour expected Monday, Nov 16.

- **Lots 27-30** · Piers nearly ready, with the pour planned for Tuesday.
- **Remaining lots** · Grading continues, with Lots 27-30 and 39-42 first so pier drilling can start on Lots 39-42 Wednesday.

The buildings



Plans · Permitted · Under construction · Complete · Not yet started

Lots 11-14

Foundation

Fourplex · 4 homes · 6704–6710 Meadowsweet Ln

Progress about 8%

Foundation Framing Roof Drywall Finishes

Backfill started Nov 9. Plumbing work is planned for Wednesday, Nov 11.

Updated Nov 9, 2026

Lots 15-18

Foundation

Fourplex · 4 homes · 6716–6722 Meadowsweet Ln

Progress about 8%

Foundation Framing Roof Drywall Finishes

Foundation walls were poured Saturday, Nov 7. Form stripping started Nov 9 and should finish by Nov 10.

Updated Nov 9, 2026

Lots 19-22

Foundation

Fourplex · 4 homes · 6728–6734 Meadowsweet Ln

Progress about 8%

Foundation Framing Roof Drywall Finishes

Wall forms move here next. The wall pour is expected Monday, Nov 16.

Updated Nov 9, 2026

Lots 23-26

Foundation

Fourplex · 4 homes · 6740–6746 Meadowsweet Ln

Progress about 8%

Foundation Framing Roof Drywall Finishes

Piers are ready. The footing pour may happen Wednesday, Nov 11.

Updated Nov 9, 2026

Lots 27-30

Foundation

Fourplex · 4 homes · 6752–6758 Meadowsweet Ln

Progress about 8%

Foundation Framing Roof Drywall Finishes

Piers should be ready to pour Tuesday, Nov 10. Grading here is the priority on Nov 10.

Updated Nov 9, 2026

Lots 31-34

Plans

Fourplex · 4 homes · 6808–6814 Meadowsweet Ln

Progress about 0%

Foundation Framing Roof Drywall Finishes

Staked by the surveyor. Grading continues under the remaining buildings.

Updated Nov 9, 2026

Lots 35-38

Plans

Fourplex · 4 homes · 6822–6828 Meadowsweet Ln

Progress about 0%

Foundation Framing Roof Drywall Finishes

Staked by the surveyor. Grading continues under the remaining buildings.

Updated Nov 9, 2026

Lots 39-42

Plans

Fourplex · 4 homes · 6834–6840 Meadowsweet Ln

Progress about 0%

Foundation Framing Roof Drywall Finishes

Grading is planned for Nov 10 so pier drilling can start Wednesday, Nov 11.

Updated Nov 9, 2026

Schedule

BUILDING	FOUNDATION	FRAMING	ROOF	DRYWALL	FINISHES
Lots 11-14 about 8% complete	In progress Started Oct 22 Plumbing planned Nov 11	*Not started*	*Not started*	*Not started*	*Not started*
Lots 15-18 about 8% complete	In progress Started Oct 22 Walls poured Nov 7	*Not started*	*Not started*	*Not started*	*Not started*
Lots 19-22 about 8% complete	In progress Started Oct 26 Wall pour target Nov 16	*Not started*	*Not started*	*Not started*	*Not started*
Lots 23-26 about 8% complete	In progress Started Oct 28 Footing pour target Nov 11	*Not started*	*Not started*	*Not started*	*Not started*
Lots 27-30 about 8% complete	In progress Started Nov 6 Pier pour target Nov 10	*Not started*	*Not started*	*Not started*	*Not started*
Lots 31-34 about 0% complete	*Not started*	*Not started*	*Not started*	*Not started*	*Not started*
Lots 35-38 about 0% complete	*Not started*	*Not started*	*Not started*	*Not started*	*Not started*

BUILDING	FOUNDATION	FRAMING	ROOF	DRYWALL	FINISHES
Lots 39-42 about 0% complete	*Not started* Pier drilling planned Nov 11	*Not started*	*Not started*	*Not started*	*Not started*

Actual dates are the first and last days the field notes record the work. Target dates appear as the master schedule fills in. Percent complete is a rough estimate by phase.

Jobsite photos




Lots 11-14 · Nov 9



Lots 11-14 · Nov 9




Lots 11-14 · Nov 9

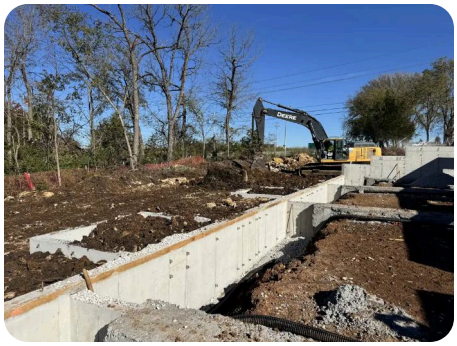

Lots 11-14 · Nov 9



Lots 15-18 · Nov 9

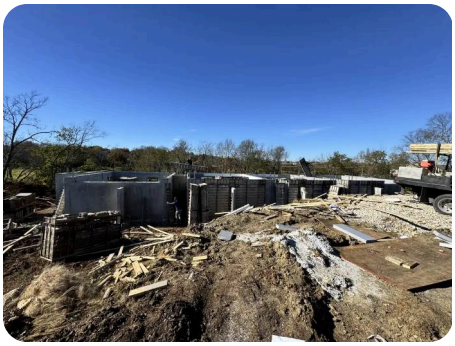

Lots 15-18 · Nov 9

Coming up

Tuesday
Nov 10

Lots 15-18
Finish stripping the wall forms

Lots 27-30
Pour foundation piers

Lots 27-30 and 39-42
Grade under the next buildings

Wednesday Nov 11	Lots 11-14	Plumbing work starts after backfill
	Lots 23-26	Pour footings
	Lots 39-42	Pier drilling starts
Monday Nov 16	Lots 19-22	Pour foundation walls
Date to be set when crews confirm	Lots 27-42	Install silt fencing along the driveways

Hidden Creek Reserve is a 59-home townhome community with a clubhouse, built in fourplex, triplex and duplex buildings. This page updates each weekday evening from the supervisor's field notes and jobsite photos.
