CONSTRUCTION UPDATE BY TYLER SUPALLA, SUPERVISOR

Hidden Creek Reserve

Townhomes in Shawnee, Kansas

Last updated Fri, Oct 30, 2026 at 11:24 AM Central

Foundation wall forms are coming off Lots 11-14 today, and pier drilling on Lots 23-26 is wrapping up ahead of a pier pour planned for Tuesday.

LATEST FROM THE SITE

Friday, October 30

- **Lots 11-14** · foundation wall forms are being stripped today. Dampproofing is scheduled for Tuesday, Nov 3, and backfill is planned for Wednesday, Nov 4.
- **Lots 23-26** · pier drilling is finishing today, with the pier pour planned for Tuesday, Nov 3, weather permitting.
- **Lots 19-22** · piers are finished; a few small piers will be filled when the footings are poured.
- **Lots 11-14** · a site meeting with the plumbing, irrigation and sewer trades is planned for Friday, Nov 6.

16	Oct 30
homes in foundation work	last site update
across 4 buildings	*from the field notes*

Weekly recap

Footings went in on Lots 15-18, wall forms started coming off Lots 11-14, and piers are done on Lots 19-22 with Lots 23-26 close behind.

THIS WEEK

- **Lots 15-18** · Footing forms installed and the footing pour started.
- **Lots 11-14** · Foundation wall forms being stripped.
- **Lots 19-22** · Piers completed, with the pier approach approved by the city inspector.
- **Lots 23-26** · Pier drilling started and is nearly finished.
- **Lots 15-26** · City approvals in place for the next three fourplexes; building permits are close to being issued.

NEXT WEEK

- **Lots 11-14** · Dampproofing on Tuesday, Nov 3, and backfill planned for Wednesday, Nov 4.
- **Lots 23-26** · Pier pour planned for Tuesday, Nov 3, weather permitting.
- **Lots 11-14** · Site meeting with the plumbing, irrigation and sewer trades on Friday, Nov 6.
- **Remaining lots** · Grading crew expected back to start grading.

The buildings

Lots 11-14

Foundation

Fourplex · 4 homes · 6704–6710 Meadowsweet Ln

Plans — Complete

Foundation wall forms were being stripped on Oct 30. Dampproofing is scheduled for Tuesday, Nov 3, with backfill planned for Wednesday, Nov 4.

Updated Oct 30, 2026

Lots 15-18

Foundation

Fourplex · 4 homes · 6716–6722 Meadowsweet Ln

Plans — Complete

Foundation piers poured. Footing forms went in on Oct 29, and the footing pour started that afternoon.

Updated Oct 29, 2026

Lots 19-22

Foundation

Fourplex · 4 homes · 6728–6734 Meadowsweet Ln

Plans — Complete

Piers are finished. A few small piers will be filled when the footings are poured.

Updated Oct 30, 2026

Lots 23-26

Foundation

Fourplex · 4 homes · 6740–6746 Meadowsweet Ln

Plans — Complete

Pier drilling is finishing up, with the pier pour planned for Tuesday, Nov 3, weather permitting.

Updated Oct 30, 2026

Schedule

BUILDING	FOUNDATION	FRAMING	ROOF	DRYWALL	FINISHES
Lots 11-14 about 8% complete	In progress Started Oct 22	*Not started*	*Not started*	*Not started*	*Not started*
Lots 15-18 about 8% complete	In progress Started Oct 22	*Not started*	*Not started*	*Not started*	*Not started*
Lots 19-22 about 8% complete	In progress Started Oct 26	*Not started*	*Not started*	*Not started*	*Not started*
Lots 23-26 about 8% complete	In progress Started Oct 28 Pier pour target Nov 3	*Not started*	*Not started*	*Not started*	*Not started*

Actual dates are the first and last days the field notes record the work. Target dates appear as the master schedule fills in. Percent complete is a rough estimate by phase.

Jobsite photos




Lots 15-18 · Oct 30, 2026



Lots 15-18 · Oct 30, 2026



Lots 11-14 · Oct 30, 2026

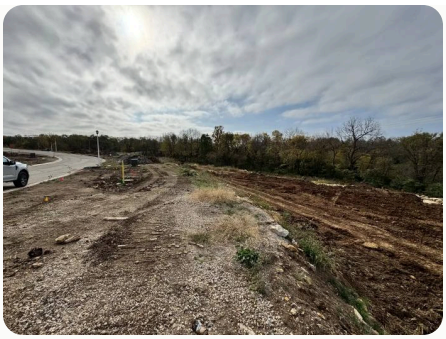

Lots 23-26 · Oct 29, 2026



Lots 23-26 · Oct 29, 2026



Lots 23-26 · Oct 29, 2026

Coming up

NOV 2
Lots 11-14
Move foundation wall forms to the next building (target)
Monday

NOV 3
Lots 11-14
Dampproof foundation walls
Tuesday

NOV 3
Lots 23-26
Pour foundation piers (weather permitting)
Tuesday

NOV 4
Lots 11-14
Backfill around the foundation (planned)
Wednesday

NOV 6
Lots 11-14
Site meeting with plumbing, irrigation and sewer trades
Friday

DATE *TBD*
Remaining lots
Grading crew returns to begin grading

Hidden Creek Reserve is a 59-home townhome community with a clubhouse, built in fourplex and duplex buildings. This page updates each weekday evening from the supervisor's field notes and jobsite photos.
