CONSTRUCTION UPDATE BY TYLER SUPALLA, SUPERVISOR

Hidden Creek Reserve

Townhomes in Shawnee, Kansas

Footing forms went in on Lots 15-18 this morning, the next step toward pouring that building's footings.

LATEST FROM THE SITE

Thursday, October 29

- **Lots 15-18** · footing forms were installed this morning.
- **Lots 15-26** · city approvals are in place and building permits are close to being issued, so work is not held up.
- **Lots 11-14** · foundation wall forms are scheduled to be stripped and moved on Friday, Oct 30.

16
homes in foundation work
across 4 buildings

Oct 29
last site update
from the field notes

Weekly recap

Foundation work is now under way on all four fourplexes, and city approvals are in place for the next three, with building permits close behind.

THIS WEEK

- **Lots 15-26** · City approvals in place for the next three fourplexes; building permits are close to being issued.
- **Lots 11-14** · Foundation wall pour scheduled, with forms set to be stripped and moved on Friday.
- **Lots 19-22** · Piers dug and completed, with the pier approach approved by the city inspector.
- **Lots 23-26** · Pier work started.
- **Lots 15-18** · Footing forms installed, ahead of the footing pour.

NEXT WEEK

- **Lots 23-26** · Target pier pour on Monday, Nov 2.
- **Remaining lots** · Grading crew expected back to start grading.

The buildings

Lots 11-14

Foundation

Fourplex · 4 homes · 6704–6710 Meadowsweet Ln

Plans — Complete

Foundation wall forms are scheduled to be stripped and moved on Friday, Oct 30. Framing lumber is staged and ready.

Updated Oct 28, 2026

Lots 15-18

Foundation

Fourplex · 4 homes · 6716–6722 Meadowsweet Ln

Plans — Complete

Foundation piers poured, and footing forms were installed on Oct 29.

Updated Oct 29, 2026

Lots 19-22

Foundation

Fourplex · 4 homes · 6728–6734 Meadowsweet Ln

Plans — Complete

Piers are done, and the city inspector approved the approach used for the piers.

Updated Oct 28, 2026

Lots 23-26

Foundation

Fourplex · 4 homes · 6740–6746 Meadowsweet Ln

Plans — Complete

Pier work is under way, with a target pier pour of Monday, Nov 2.


Updated Oct 28, 2026

Schedule

BUILDING	FOUNDATION	FRAMING	ROOF	DRYWALL	FINISHES
Lots 11-14 about 8% complete	In progress Started Oct 22	*Not started*	*Not started*	*Not started*	*Not started*
Lots 15-18 about 8% complete	In progress Started Oct 22	*Not started*	*Not started*	*Not started*	*Not started*
Lots 19-22 about 8% complete	In progress Started Oct 26	*Not started*	*Not started*	*Not started*	*Not started*
Lots 23-26 about 8% complete	In progress Started Oct 28 Pier pour target Nov 2	*Not started*	*Not started*	*Not started*	*Not started*

Actual dates are the first and last days the field notes record the work. Target dates appear as the master schedule fills in. Percent complete is a rough estimate by phase.

Jobsite photos

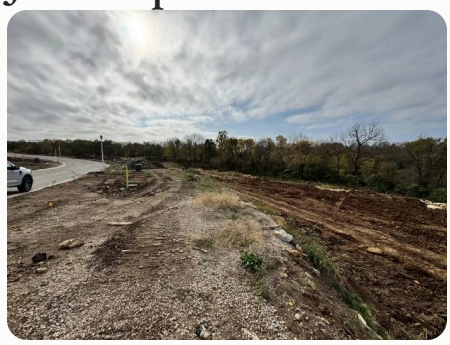

Lots 23-26 · Oct 29, 2026



Lots 23-26 · Oct 29, 2026



Lots 23-26 · Oct 29, 2026



Lots 19-22 · Oct 29, 2026



Lots 19-22 · Oct 29, 2026



Lots 15-18 · Oct 29, 2026

Coming up

OCT 30

Lots 11-14
Strip and move foundation wall forms
Friday

NOV 2

Lots 23-26
Pour foundation piers (target)
Monday

DATE *TBD*

Lots 15-18
Pour foundation footings

DATE *TBD*

Remaining lots
Grading crew returns to begin grading

Hidden Creek Reserve is a 59-home townhome community with a clubhouse, built in fourplex and duplex buildings. This page updates each weekday evening from the supervisor's field notes and jobsite photos.
