CONSTRUCTION UPDATE BY TYLER SUPALLA, SUPERVISOR

Hidden Creek Reserve

Townhomes in Shawnee, Kansas

Last updated Fri, Nov 6 at 1:52 PM Central

The Lots 15-18 wall pour is planned for Saturday, piers are ready on Lots 23-26, and pier drilling starts today on Lots 27-30.

LATEST FROM THE SITE

Friday, November 6

- **Lots 15-18** · crews are finishing the wall forms. The wall pour, about four hours, is planned for Saturday.
- **Lots 23-26** · piers are ready, and the footing pour is hoped for Monday.
- **Lots 27-30** · the building is being marked out and pier drilling starts today. The pier pour may be next Wednesday.
- Lots 11-14 and remaining lots: backfill and more grading under the next buildings start Monday, and the utility and plumbing trades meet on site Monday afternoon.

20
homes under construction
in 5 buildings, all at the foundation stage

Nov 7
Pour foundation walls
Lots 15-18, saturday

Weekly recap

Foundation work moved forward on five buildings despite rain, with dampproofing on Lots 11-14, wall forms ready on Lots 15-18, footing and pier work on Lots 19-26, and the next four buildings staked and graded.

THIS WEEK

- **Lots 11-14** · Dampproofing started Wednesday, and gravel for the slab base was delivered Thursday.
- **Lots 15-18** · Wall forms nearly finished after rain slowed work. The wall pour is planned for Saturday.
- **Lots 19-22** · Footing forms went in Wednesday, and the footing pour was scheduled for Thursday afternoon.

NEXT WEEK

- **Lots 11-14** · Backfill Monday, with plumbing work resuming Wednesday.
- **Lots 23-26** · Footing pour hoped for Monday.
- **Lots 27-30** · Pier pour possibly Wednesday.
- **Remaining lots** · Grading resumes Monday, and utility and plumbing trades meet on site.

- **Lots 23-26** · Pier drilling wrapped up after rain delays, and the piers are ready for footings.
- **Lots 27-42** · All four buildings staked by the surveyor and grading started Wednesday. Lots 27-30 marked out, with pier drilling starting Friday.

The buildings



Plans · Permitted · Under construction · Complete · Not yet started

Lots 11-14

Foundation

Fourplex · 4 homes · 6704–6710 Meadowsweet Ln

Progress about 8%

Foundation Framing Roof Drywall Finishes

Gravel for the slab base is on site. Backfill is planned for Monday, Nov 9, with plumbing work resuming Wednesday, Nov 11.

Updated Nov 6, 2026

Lots 15-18

Foundation

Fourplex · 4 homes · 6716–6722 Meadowsweet Ln

Progress about 8%

Foundation Framing Roof Drywall Finishes

Crews are finishing the wall forms. The wall pour, about four hours, is planned for Saturday, Nov 7.

Updated Nov 6, 2026

Lots 19-22

Foundation

Fourplex · 4 homes · 6728–6734 Meadowsweet Ln

Progress about 8%

Foundation Framing Roof Drywall Finishes

Piers are finished. The footing pour is scheduled for Nov 5.

Updated Nov 5, 2026

Lots 23-26

Foundation

Fourplex · 4 homes · 6740–6746 Meadowsweet Ln

Progress about 8%

Foundation Framing Roof Drywall Finishes

Piers are ready. The footing pour is hoped for Monday, Nov 9.

Updated Nov 6, 2026

Lots 27-30

Foundation

Fourplex · 4 homes · 6752–6758 Meadowsweet Ln

Progress about 8%

Foundation Framing Roof Drywall Finishes

The building is being marked out and pier drilling starts Nov 6. The pier pour may be Wednesday, Nov 11.

Updated Nov 6, 2026

Lots 31-34

Plans

Fourplex · 4 homes · 6808–6814 Meadowsweet Ln

Progress about 0%

Foundation Framing Roof Drywall Finishes

Staked by the surveyor. Grading started Nov 4 and resumes Monday, Nov 9.

Updated Nov 6, 2026

Lots 35-38

Plans

Fourplex · 4 homes · 6822–6828 Meadowsweet Ln

Progress about 0%

Foundation Framing Roof Drywall Finishes

Staked by the surveyor. Grading started Nov 4 and resumes Monday, Nov 9.

Updated Nov 6, 2026

Lots 39-42

Plans

Fourplex · 4 homes · 6834–6840 Meadowsweet Ln

Progress about 0%

Foundation Framing Roof Drywall Finishes

Staked by the surveyor. Grading started Nov 4 and resumes Monday, Nov 9.

Updated Nov 6, 2026

Schedule


BUILDING	FOUNDATION	FRAMING	ROOF	DRYWALL	FINISHES
Lots 11-14 about 8% complete	In progress Started Oct 22 Backfill planned Nov 9	*Not started*	*Not started*	*Not started*	*Not started*
Lots 15-18 about 8% complete	In progress Started Oct 22 Wall pour target Nov 7	*Not started*	*Not started*	*Not started*	*Not started*
Lots 19-22 about 8% complete	In progress Started Oct 26 Footing pour scheduled Nov 5	*Not started*	*Not started*	*Not started*	*Not started*
Lots 23-26 about 8% complete	In progress Started Oct 28 Footing pour target Nov 9	*Not started*	*Not started*	*Not started*	*Not started*
Lots 27-30 about 8% complete	In progress Started Nov 6 Pier pour target Nov 11	*Not started*	*Not started*	*Not started*	*Not started*
Lots 31-34 about 0% complete	*Not started*	*Not started*	*Not started*	*Not started*	*Not started*
Lots 35-38 about 0% complete	*Not started*	*Not started*	*Not started*	*Not started*	*Not started*
Lots 39-42 about 0% complete	*Not started*	*Not started*	*Not started*	*Not started*	*Not started*

Actual dates are the first and last days the field notes record the work. Target dates appear as the master schedule fills in. Percent complete is a rough estimate by phase.

Jobsite photos



Lots 11-14 · Nov 5

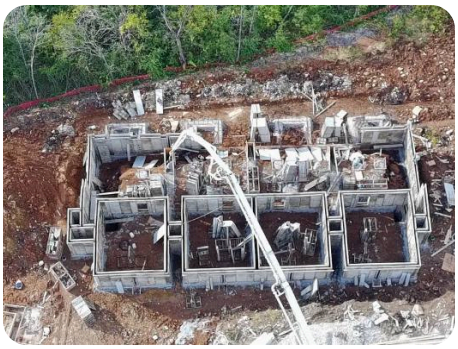

Lots 15-18 · Nov 5



Lots 15-18 · Nov 5



Lots 19-22 · Nov 5



Lots 23-26 · Nov 5



Lots 11-14 · Nov 4

Coming up

Saturday
Nov 7

Lots 15-18
Pour foundation walls

Monday
Nov 9

Lots 11-14
Backfill around the foundation

Lots 23-26
Pour footings

Remaining lots
Grading resumes under the next buildings

Site
Utility and plumbing trades meet on site

Wednesday Nov 11	Lots 11-14 Plumbing work resumes after backfill Lots 27-30 Pour foundation piers
Date to be set when crews confirm	Lots 27-42 Install silt fencing along the driveways

Hidden Creek Reserve is a 59-home townhome community with a clubhouse, built in fourplex, triplex and duplex buildings. This page updates each weekday evening from the supervisor's field notes and jobsite photos.
